

Street Name Sign Project

2013 - 2015

Update at July 2015

**Inc. Village of Plandome Heights
Street Name Sign Program**

There are compelling reasons to move forward to replace our decorative Street Name Signs with new reflective signs. These include:

- All signs need to be reflective by, I believe, 2016,
- We are behind our peers; our neighbors in Plandome, Plandome Manor, Flower Hill, as well as unincorporated Manhasset, are compliant with the reflective signs now,
- We now have repeatable process for “hardening” poles and signs through design and trial & error over an 18 month period,
- We have the will and capacity to execute, in both staff and an in-place vendor,
- We have surplus funds (and other means) to do the project,
- We have the “volunteer capital” to move now.

The project is can be staged according to priorities and availability of funds as follows:

Key: Priority Groups are:
1 = Very high traffic, main artery - DONE
2 = High traffic, thru streets - NEXT
3 = Interior
4 = Interior low traffic


A summary of this project, past, present and proposed follows:

<u>Program summary</u>	<u>Signs</u>	<u>Post</u>	<u>Cost/Est Cost</u>	<u>Status</u>
Done 2013 -14, priority 1	6	4	2,163	Done, Prior Year
Fiscal 2014-15, priority 1	8	3	1,860	Done, Current Year
Subtotal, priority 1	14	7	4,023	DONE
Fiscal 2014 -15, priority 2	10	1	1,945	DONE
Fiscal 2014 -15, priority 3	11	1	2,125	DONE
Fiscal 2015-16	17	0	3,060	Next
Program	52	9	11,153	3 yr. program

A map of the program and details of the program are enclosed.

1 = Very high traffic, main artery
2 = High traffic, thru streets
3 = Interior
4 = Interior low traffic

4 = Interior low traffic

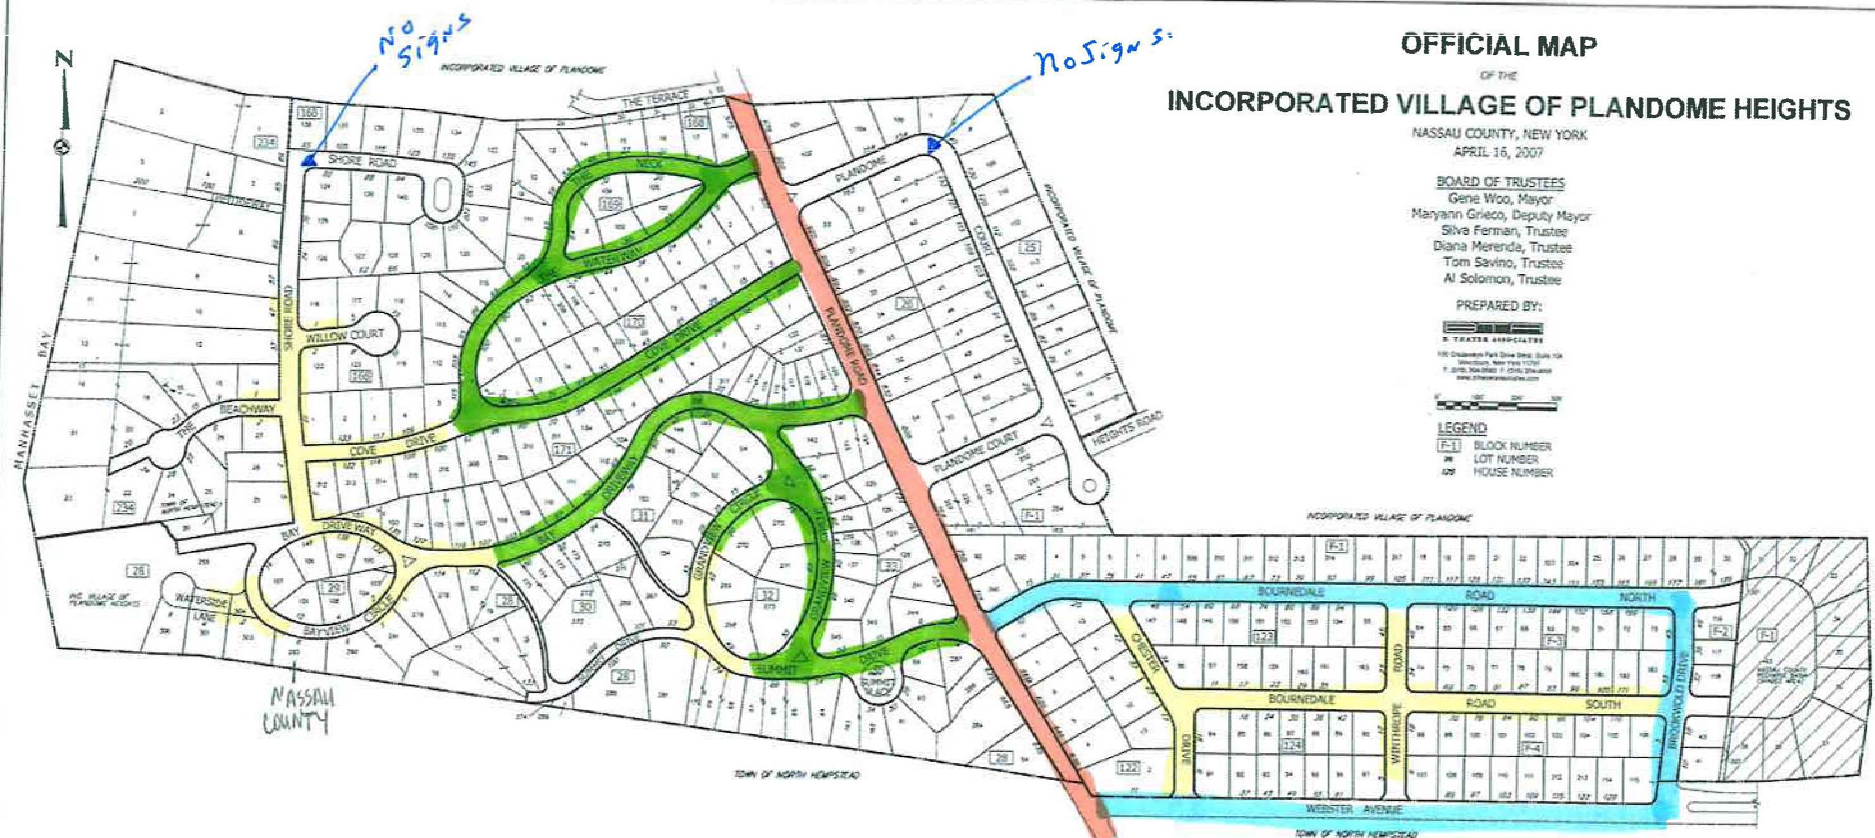

Inc. Village of Plandome Heights
Street Identity Signs - Project Details

Key: Priority Groups are:

1 = Very high traffic, main artery
 2 = High traffic, thru streets
 3 = Interior
 4 = Interior low traffic

<u>Program summary</u>	<u>Signs</u>	<u>Post</u>	<u>Cost/Est Cost</u>	<u>Status</u>
Done prior year, priority 1	6	4	2,163	Done, PY
Fiscal 2014-15, priority 1	8	3	1,860	Done, CY
Subtotal, priority 1	14	7	4,023	DONE
Fiscal 2014 -15, priority 2	10	1	1,945	DONE
Fiscal 2014 -15, priority 3	11	1	2,125	DONE
Fiscal 2015-16	17	0	3,060	Next
Program	52	9	11,153	3 yr. program

<u>Grp</u>	<u>Loc.</u>	<u>Street</u>	<u>@</u>	<u>Street</u>	<u>Signs</u>	<u>Post</u>	<u>Comments</u>
				Plandome Court N	2	1	Done 2013
1	1	Plandome Road	@	Plandome Court S	2	1	Done 2013
1	2	Plandome Road	@	The Waterway/The Neck	2	1	Done Spring 2014
1	3	Plandome Road	@	Cove Drive	2	1	Done, Fall 2014
1	4	Plandome Road	@	Bournedale Road North	2	1	Done, Fall 2014
1	5	Plandome Road	@	Bay Driveway	2	1	Done Fall 2014
1	6	Plandome Road	@	Summit Drive	2	1	Done Fall 2014
1	7	Plandome Road	@		14	7	
				Chester Drive	2	0	Done Spring 2015
2	8	Webster Avenue	@	Winthrop Road	2	0	Done Spring 2015
2	9	Webster Avenue	@	Brookwold Drive	2	1	Loc. gets vandals
2	10	Webster Avenue	@	Bournedale Road South	2	0	Done Spring 2015
2	11	Brookwold Drive	@	Bournedale Road North	0	0	Done Spring 2015
2	12	Brookwold Drive	@	Winthrop Road	0	0	Done Spring 2015
2	13	Bournedale Road North	@	Chester Drive	2	0	Done Spring 2015
2	14	Bournedale Road North	@		10	1	
			@	Grandview Circle	2	1	Pole is oddball
3	15	Bay Driveway	@	Grandview Circle	2	0	Done Sum. 2015
3	16	Grandview Circle	@	Summit Drive	2	0	Done Sum, 2015
3	17	Grandview Circle	@	The Neck	2	0	Done Sum. 2015
3	18	The Waterway	@	The Neck	2	0	Done Sum. 2015
4	19	The Waterway	@	Cove Drive	1	0	Needs Cove Drive
4	20	The Waterway	@		11	1	
				Bayview Circle	2	0	
4	21	Bay Driveway	@	Bay Driveway	2	0	
4	22	Shore Road	@	Cove Drive	2	0	
4	23	Shore Road	@	Willow Court	2	0	
4	24	Shore Road	@	The Beachway	2	0	
4	25	Shore Road	@	The Tideway	2	0	
4	26	Shore Road	@	The Beachway	2	0	
4	27	Shore Road	@	Chester Drive	2	0	
							Needs Winthrop
4	28	Bournedale Road South	@	Winthrop Road	1	0	Road
4	29	Bournedale Road South	@		17	0	
				Total program	52	9	
